

IKeriKin

I Care for Your Kin — Project Implementation Plan


Team activity: Project Timeline, Milestones, and Risk Assessment (Week 2 Progress Presentation)

Project duration: 11 weeks — Mon, Jul 13, 2026 to Sun, Sep 27, 2026

Repository: github.com/LorenzoBrentReedVarca/IKeriKin

1. Project Timeline / Gantt Chart

The project is organized into 7 phases across 11 weeks, from initiation to final presentation. Detailed tasks and subtasks, with start/end dates and durations, are listed below the chart.

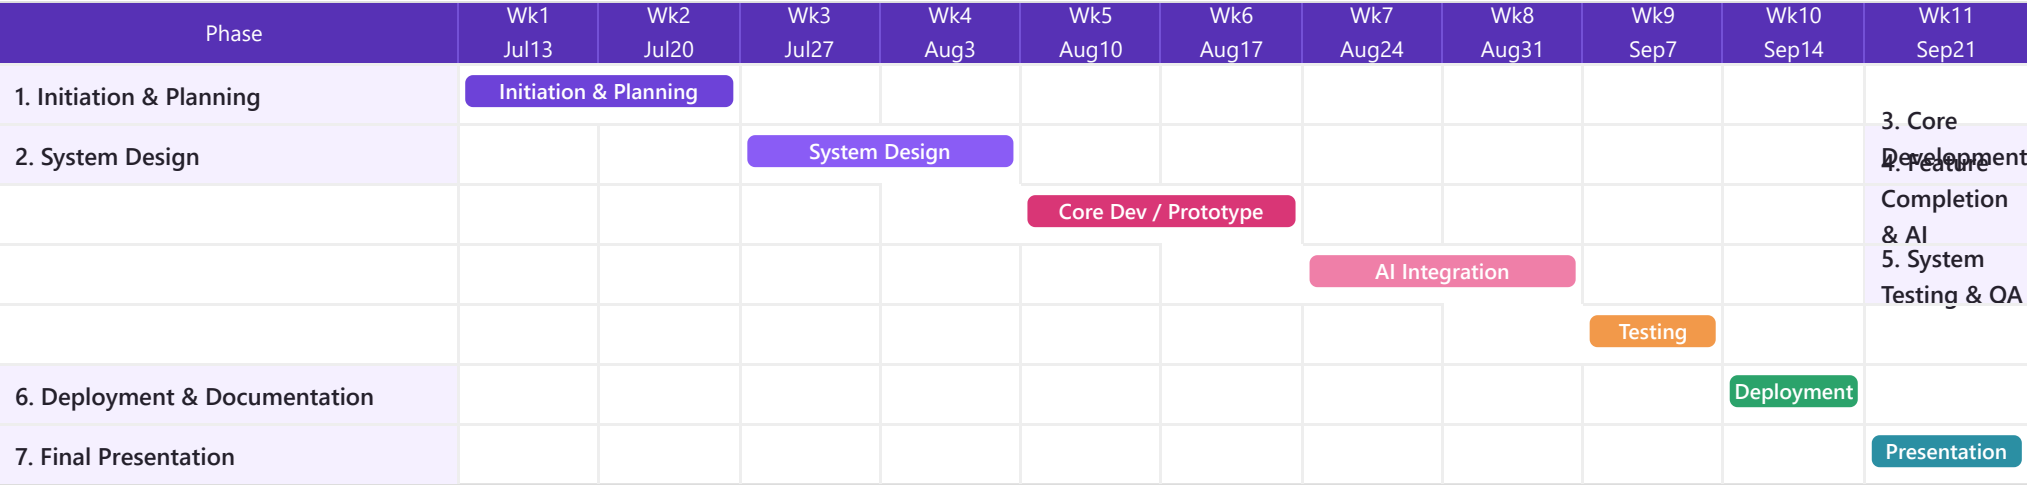

Detailed Task Breakdown

Phase	Task / Subtask	Start Date	End Date	Duration
1. Initiation & Planning	Requirements gathering & problem definition	Jul 13	Jul 15	3 days
	Target-user & SPED needs research	Jul 13	Jul 16	4 days
	Revise and finalize project proposal	Jul 16	Jul 19	4 days
	Set up Flutter project & layered architecture (presentation/domain/data/application/core)	Jul 14	Jul 17	4 days
	Define system architecture & tech stack (Riverpod, GoRouter, Supabase)	Jul 17	Jul 19	3 days
	Progress report, screenshots & Week 2 submission	Jul 20	Jul 26	7 days
2. System Design	UI/UX wireframes for the 5 core screens	Jul 27	Jul 31	5 days

	Design system: Material 3 theme + accessibility spec	Jul 29	Aug 2	5 days
	Database schema design (users, children, lessons, progress)	Jul 30	Aug 3	5 days
	API / Edge Function design for AI lesson generation	Aug 3	Aug 6	4 days
	Navigation architecture (GoRouter + responsive nav shell)	Aug 3	Aug 6	4 days
	Design review & documentation sign-off	Aug 7	Aug 9	3 days
3. Core Development / Prototype	Implement auth (registration, login, recovery, offline preview)	Aug 10	Aug 14	5 days
	Implement child profile CRUD & learner-context fields	Aug 10	Aug 15	6 days
	Build Home screen + responsive navigation shell	Aug 13	Aug 17	5 days
	Integrate Riverpod state management across screens	Aug 14	Aug 19	6 days
	Build AI Lesson Generator screen (form & inputs)	Aug 18	Aug 21	4 days
	Internal prototype demo & review	Aug 22	Aug 23	2 days
4. Feature Completion & AI Integration	Integrate Supabase Edge Function for AI lesson generation	Aug 24	Aug 28	5 days
	Build stories, flashcards & quizzes	Aug 24	Aug 29	6 days
	Build memory & matching games	Aug 27	Aug 31	5 days
	Implement text-to-speech for stories	Aug 31	Sep 2	3 days
	Implement Progress Dashboard (weekly/monthly/all-time)	Sep 1	Sep 4	4 days
	Implement XP, coins, streaks & badges	Sep 2	Sep 5	4 days
	Implement accessibility settings (text size, contrast, reduced motion)	Sep 4	Sep 6	3 days
5. System Testing & QA	Unit tests (domain & data layers)	Sep 7	Sep 8	2 days
	Widget tests for the 5 core screens	Sep 8	Sep 10	3 days
	Integration testing (auth + Supabase + Edge Functions)	Sep 9	Sep 11	3 days

IKeriKin - Project Implementation Plan

	Accessibility & usability testing	Sep 10	Sep 12	3 days
	Bug fixing & performance tuning	Sep 11	Sep 13	3 days
6. Deployment & Documentation	Final bug fixes & code cleanup	Sep 14	Sep 15	2 days
	Build & verify Android/iOS/Web/Desktop releases	Sep 15	Sep 17	3 days
	Finalize documentation (README, proposal PDF, screenshots)	Sep 16	Sep 18	3 days
	Deploy web build / prepare release artifacts	Sep 18	Sep 20	3 days
7. Final Presentation	Prepare final presentation slide deck	Sep 21	Sep 23	3 days
	Prepare live demo script & rehearse	Sep 23	Sep 25	3 days
	Final presentation & documentation submission	Sep 26	Sep 27	2 days

2. Milestones and Deliverables

Milestone	Expected Output	Target Date
Project Proposal Approved	Approved Proposal	Week 2
System Design Completed	Design Documents	Week 4
Prototype Finished	Functional Prototype	Week 6
System Testing	Test Report	Week 8
Final System Completed	Completed System	Week 10
Final Presentation	Presentation & Documentation	Week 11

3. Risk Assessment and Contingency Plan

Risk	Impact	Contingency Plan
Team member unavailable (illness, exams, personal issues)	Medium	Reassign tasks to other members; keep architecture and progress documented so any member can pick up a layer (presentation/domain/data/application)
Delay in AI/Supabase Edge Function integration	High	Build a local/mock lesson generator fallback first; adjust the schedule and prioritize core offline features over AI polish
Internet connectivity issues (Supabase requires network access)	Medium	Rely on the existing offline preview mode (SharedPreferences); prepare offline demo copies and a backup mobile hotspot for presentations
Hardware failure or device loss	High	Commit and push code to GitHub frequently; store data in Supabase (cloud); keep a secondary test device/emulator available
Scope changes / feature creep	High	Lock the core feature list after the design phase; require adviser approval before adding new features; maintain a change-request log
Sensitive child data privacy (disability, health & learning information)	High	Store only necessary data, use Supabase Auth and row-level security, follow the Data Privacy Act, and avoid collecting identifiable data beyond what is needed
Cross-platform UI inconsistencies (Android/iOS/Web/Desktop)	Medium	Use the shared ResponsiveGrid/ResponsiveBody widgets, test on multiple screen sizes each sprint, and run <code>flutter analyze/flutter test</code> before every merge
AI-generated content inaccurate or inappropriate for a child's needs	High	Add a content-review step and prompt guardrails tailored to each disability/learning profile; fall back to curated templates if AI output fails validation
